

WeLearn Growth Hub

One learning platform for every WeLearn cohort, bringing together Edmentum, the PBL/STEAM simulations and other learning materials: what we will build, what we need, and in what order.

Version 2 · **Date:** 25 September 2026 · **Status:** Proposal for school review · **Audience:** School leadership, IT, teaching leads

Contents

1	Summary	2
2	Where WeLearn is today	2
3	Review of the supplied wireframes	3
4	How it fits together	4
5	Who does what	4
6	Implementation phases	4
7	What the school needs to do	7
8	Questions for Edmentum	8
9	Costs	8
10	Main risks	8
11	Next steps	9

1. Summary

WeLearn Growth Hub will be a single learning platform for all of our cohorts. Students open their Edmentum courses, the WeLearn PBL/STEAM simulations and other materials in one place, and staff, teachers and parents each see what they need.

Cohort	Learners	What the platform provides for them
W2E	Twice-exceptional (2e) learners, secondary	A learning profile per student with accommodations (extended time, reduced visual load, text-to-speech, tasks broken into steps), stretch challenges that build on strengths, and support notes visible only to that student's teachers.
WPR	International students, primary	A simpler, age-appropriate interface; accounts activated only after verified parental consent; English/Chinese/Thai throughout; AI tutor limited or off by default for younger children.
All cohorts	Every learner	One sign-in, My Courses, gradebook and transcripts, parent portal, mobile-friendly and accessible design.

Dual programme: Thai Diploma. Every cohort can also take the Thai Diploma alongside their main programme. It is taught by a Thai Diploma teacher: students open WeLearn Growth Hub and access the learning materials, lessons and assignments the teacher publishes, in Thai. Each student's record shows their main programme and the Thai Diploma side by side, with a separate Thai Diploma transcript.

Recommendation. Build these LMS functions into WeLearn itself and roll them out in stages, starting with a one-class pilot. The build takes an estimated **5–6 months**, needs **no outside development company**, and needs no LMS licence. In exchange, the school takes on ownership: a named staff member, a hosting bill, and a security review before launch.

What we (the build team) deliver

- Admin console: staff, student and parent accounts, schools, classes
- Student "My Courses" home: Edmentum, simulations and materials together
- One-click Edmentum launch with grades returned (LTI 1.3)
- Teacher gradebook, terms and transcripts
- Public course guidebook: our full catalogue of partner-school courses, searchable by families
- Parent portal, English/Chinese/Thai, mobile-friendly

What the school must provide

- Approval of this plan and funding for its costs
- Confirmation of the Platform Lead role, with protected time
- Firebase **Blaze** billing plan
- A sending mailbox in our existing Microsoft 365
- Edmentum registration details for WeLearn (LTI 1.3)
- A security & privacy review before launch

2. Where WeLearn is today

Area	Status	Notes
------	--------	-------

Student and coach dashboards (React)	BUILT	Modern component-based front end.
Secure roles and class-level data privacy	BUILT	Roles cannot be faked; teachers see only their own classes. Covered by automated tests.
Class join codes	BUILT	Students enrol themselves safely with a code like G7PR-Q966.
PBL/STEAM simulations	BUILT	Solar Car (real measurements) and SO ₂ model among six activities.
AI tutor and hints	LOCAL ONLY	Works on a developer machine; not live , because no backend is deployed.
Backend server in production	MISSING	Blocks the admin console, Edmentum and AI. Needs the Blaze plan.
Admin console, schools, parents, gradebook, Edmentum	MISSING	The subject of this plan.


3. Review of the supplied wireframes

The 20 "EduBiz Gateway System" wireframes were reviewed. They are a good specification for the **admin side**, but they describe an education-agency back office (enquiries, course bookings, accreditations, student balances), not an LMS. They contain no student course view, no Edmentum launch, no assignments and no gradebook, which are the parts students and teachers use most.

Decision	Wireframe screens
Keep	Staff / student / parent account lists, create, edit, suspend, account history, change email, settings, password reset, language settings (extended to English, Chinese and Thai).
Redesign	Parent linking (typing an email lets anyone attach to any child → replace with one-time invite codes). Student photos (optional, off by default, location data stripped). Public "Client Viewable" reviews (moderated, with consent, or removed).
Keep, with the catalogue	Education Providers, Accreditations and course reviews: part of the course catalogue and public guidebook (Phase C).
Later (Phase G)	Enquiries, Course Bookings and student balances: part of buying courses and study paths after go-live.
Add	My Courses, Edmentum launch, assignments, gradebook, terms/transcripts, teacher class view, parent portal.

Data inconsistencies in the mock-ups have been fixed in our designs. Examples: the same User ID assigned to three different people, a parent shown with 0 students who has 2, and "page 1 of 3" for 129 records. One mock-up student is 12: with the WPR primary cohort, under-13 learners are in scope, and the plan provides the parental consent this requires (Phase E).

4. How it fits together

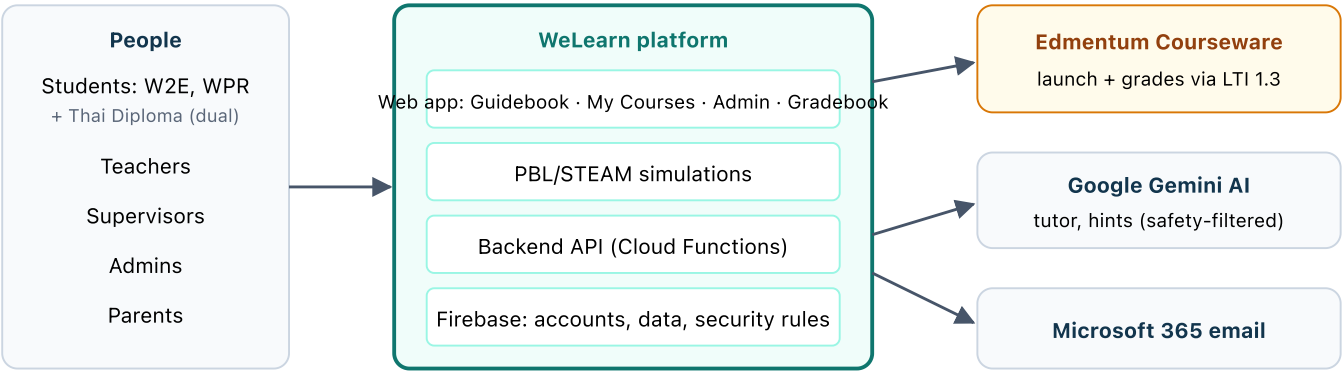

LTI 1.3 is the published education standard that lets an LMS open an outside course tool with one click (no second login) and receive grades back. Edmentum states it supports "any LMS that supports LTI 1.3". WeLearn will implement the LMS side of that standard.

5. Who does what

Role	Responsibilities
David Doran Founder & CEO, Project Sponsor	Approves the plan, oversees the build through milestone updates, and funds the project and its running costs.
Mani Golzary AI Learning Architect & Platform Lead	Designs the platform and its learning experience, and leads the build end to end: sets the architecture and roadmap, directs and reviews the AI build team, and approves every production release and data migration. Accountable day to day for student data security; manages Edmentum and service providers; reports progress to the CEO at each milestone; trains teachers and turns their feedback into product decisions.
Claude (AI, front end)	All screens and user experience: admin console, My Courses, gradebook, parent portal, accessibility, mobile, English/Chinese/Thai. Verifies features against the running system, not just a successful build.
Gemini (AI, back end)	Server API, deployment, database rules, data migration, Edmentum LTI connection, email delivery. Works to a written API contract so both sides fit.
Outside specialists (one-off)	Independent security test and privacy/legal review before real student data goes live.

Why human accountability is essential. On this project, AI-built features have been reported as working when they were not: data was silently failing to save, and only checking the live system caught it. AI does the building; a person must approve releases and answer for the platform.

6. Implementation phases

Durations are estimates for the build team and assume the school's inputs (section 7) arrive on time. Edmentum registration runs in parallel and should be started early.

Phase 0 · Front-end groundwork

Weeks 1–4 · **CAN START NOW**

- Admin console layout with WeLearn branding, role-aware navigation and a reusable data table
- Staff, student and parent account screens, built against test data until the backend is live
- Settings (change password, language) and password reset. These **work for real immediately**.
- First version of the student "My Courses" page and the parent portal screens

Phase A · Backend, roles, cohorts and schools

3–4 weeks once Blaze is on

- Deploy the backend server; the AI tutor becomes live in production
- Roles: admin, supervisor, course coordinator (teacher), student, parent
- Organisation → cohorts (W2E, WPR) → schools → classes structure, with a safe migration of existing accounts
- Dual enrolment: any student in any cohort can also be enrolled in the Thai Diploma
- Admin actions (create, edit, suspend, change email) with a tamper-proof account history

Needs: [Blaze plan](#) · [Microsoft 365 sending mailbox](#) · [Platform Lead approval before production migration](#)

Phase B · Edmentum connection (LTI 1.3)

3–4 weeks

- Built and tested first against the free official LTI reference tool, so work is not blocked on Edmentum
- One-click launch from My Courses; teachers place Edmentum content into WeLearn courses
- Edmentum scores flow back into WeLearn automatically

Needs: [Edmentum registration details](#) · [confirmation that licences cover our students](#)

Phase C · Course catalogue, My Courses and cohort experiences

about 5 weeks

- Courses, subjects and year levels as data, not hard-coded pages
- Each course has a provider (Edmentum, WeLearn PBL, or teacher-led) and curriculum standards (e.g. NGSS, and the Thai national curriculum for the Thai Diploma)
- Standards-coverage report for leadership
- Full course editor: education provider, year levels, subjects, length, delivery type, credits, prerequisites, fees, accreditations, teachers, "featured", and a review status, with every text field translatable
- Import of our existing catalogue of about 1,030 partner-school courses into a review queue: AI drafts the clean-up and Thai/Chinese translations, and a staff member approves each course
- Public course guidebook: search and filters (provider, subject, grade, accreditation, length) and a page for every course
- Primary-friendly student interface for WPR: larger targets, simpler navigation, read-aloud
- W2E learning profiles and accommodations applied automatically across courses and simulations
- Teacher-led courses: teachers upload learning materials (documents, videos, links), organise them into units and lessons, and set assignments. The Thai Diploma is the first, with a full Thai-language interface

Phase D · Gradebook, terms and transcripts

about 4 weeks

- Terms (the wireframes' "transcript periods"), teacher gradebook combining Edmentum scores and PBL rubric scores
- Transcript export per student: main programme and a separate Thai Diploma transcript in the format it requires

Phase E · Parent portal and parental consent

about 3 weeks

- Verified parental consent before any primary (WPR) account is activated, with consent records kept
- Parents link to a child with a one-time invite code from the school; read-only progress and grades
- Optional weekly email summary in English or Chinese

Phase F · Launch readiness

2–3 weeks


- Independent security test and fixes; privacy review; staff training material
- Pilot with one W2E class first; WPR primary classes join once parental consent is live; then all cohorts after sign-off

Phase G · Buy Course and study paths (after go-live)

3–4 weeks, after the pilot

- "Buy Course" on the guidebook: online payment or an enquiry to our team, as the school decides
- "Add to Path": each student's personal study plan combining courses, e.g. partner-school courses alongside the Thai Diploma
- Enquiries and course bookings managed in the admin console

Indicative timeline (weeks)

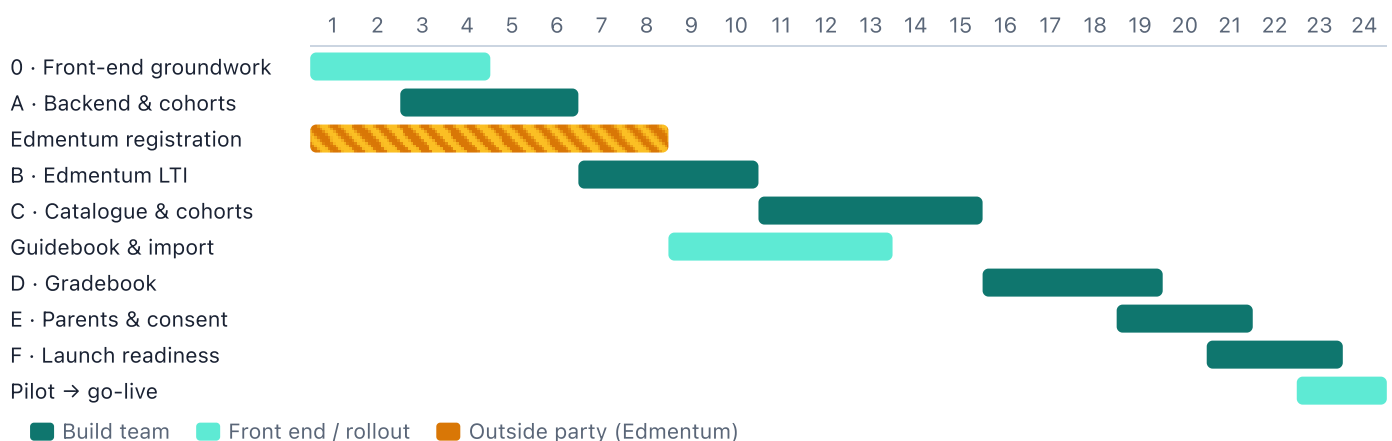

7. What the school needs to do

#	Action	Who	When	It unblocks
1	Approve the plan and budget , and confirm Mani Golzary as Platform Lead with agreed terms and protected time	David Doran (CEO)	Now	Every production release
2	Upgrade Firebase to the Blaze plan (pay-as-you-go billing)	Firebase billing owner	Before Phase A	Backend, admin console, AI in production
3	Register WeLearn with Edmentum as an LTI 1.3 LMS and obtain the connection details; get written answers to the questions in section 8; confirm licence numbers; sign a data-processing agreement	Edmentum account contact	Now	Phase B
4	Set up sending from Microsoft 365: a no-reply shared mailbox and an app registration allowed to send only from it (Microsoft Graph)	Microsoft 365 admin	Before Phase A ends	Account activation emails
5	Supply the Firebase admin key securely to the platform lead (never by email or chat)	Firebase owner	Phase A	Setting up first admin accounts
6	List the tools and features teachers rely on daily	Teaching leads	Within 2 weeks	Build order; go-live readiness
7	Commission a security test and privacy review , covering parental consent for primary learners and 2e support data	Leadership	Book by week 12	Go-live
8	Define the Thai Diploma course: subjects, credits, grading, assessment and transcript requirements, and who awards the diploma	Academic lead with the Thai Diploma teacher	Before Phase C	Thai Diploma catalogue and transcripts
9	Native Thai speaker review of the Thai interface and messages	Thai-speaking staff member	Phase C	Thai Diploma go-live
10	Export the existing course data (about 1,030 courses) from the previous WeLearn course system	Platform Lead with the previous developer	Before Phase C	Course import
11	Staff time to approve imported courses , and confirm with partner schools which courses and prices are still current	Course coordinators	Phase C onward	Public guidebook
12	Decide how "Buy Course" works (online payment or enquiry) and what a study path contains	Platform Lead, approved by the CEO	Before Phase G	Phase G

8. Questions for Edmentum

To confirm in writing with our Edmentum contact as part of action 3.

#	Question	Why it matters
1	Grade return: does LTI Assignment and Grade Services work with a custom LTI 1.3 platform such as WeLearn?	Lets Edmentum scores appear in the WeLearn gradebook automatically (Phase D).
2	Content selection: does LTI Deep Linking work with a custom LTI 1.3 platform?	Lets teachers choose Edmentum lessons and place them inside WeLearn courses (Phase B).
3	Primary learners: which Edmentum products for primary-age students are available over LTI?	Courseware is designed for grades 6–12; this decides what our WPR cohort can use.

9. Costs

Item	Type	Notes
LMS licence	None	WeLearn is the school's own platform; no per-user licence fee.
Firebase hosting, database, server	Monthly, usage-based	Small at a single school's scale; the back-end team will provide an estimate for 500 students.
Google Gemini AI	Monthly, usage-based	Rate-limited per student to cap spend.
Microsoft 365 email	Existing	Uses our current Microsoft 365; a shared no-reply mailbox needs no extra licence.
Edmentum Courseware	Existing	Unchanged; licences are bought from Edmentum as today.
Online payment fees (Phase G)	Per transaction	Only if "Buy Course" takes payments online; set by the payment provider chosen.
File storage for learning materials	Monthly, usage-based	Documents and videos uploaded by teachers (Firebase Storage); small unless large volumes of video are hosted.
Security test and privacy review	One-off	Obtain quotes; the main external spend of the project.
Platform Lead time	Ongoing	Protected time during the build; ongoing maintenance and support afterwards.

10. Main risks

Risk	Mitigation
Primary learners' data and 2e support notes are especially sensitive	Parental consent before activation; support notes visible only to the learner's own teachers; privacy review covers both.

Children's data exposed by a defect	Automated security-rule tests, server-side audit log, independent security test before go-live.
Features reported done that do not work	"Done" means verified on the running system; Platform Lead approves every release; CEO receives milestone updates; pilot with one class first.
Outside services change (AI model retired, library updates)	Settings, not code, control the AI model; monthly maintenance by the Platform Lead.
The platform depends on one person	Documentation and handover material maintained throughout, so another engineer could take over.

11. Next steps

1. School reviews and approves this plan.
2. School starts actions 1 and 3 now; these have the longest lead times.
3. Build team starts **Phase 0** immediately, since it needs nothing from the school.
4. Phase A starts as soon as the Blaze plan is active.

Source: Edmentum integrations (edmentum.com/support/integrations). Timeline and effort figures are estimates, not commitments.
